DEPARTMENT OF THE NAVY
COMMANDER FLEET ACTIVITIES
SASEBO, JAPAN
PSC 476 BOX 1
FPO AP 96322-0001

5090
Ser 00/0800
October 18, 2019

All Parents or Caregivers
Darby Elementary School

Dear Parent or Caregiver:

SUBJECT: DRINKING WATER AT DARBY ELEMENTARY SCHOOL

The safety and wellness of children at our Child Development Centers (CDC), Schools and Youth Centers (YC) are my top priority. In my earlier letter announcing our lead in drinking water testing program, I informed you that we are testing all water outlets that could potentially be used for cooking, washing or drinking at our CDCs and YCs.

This week, we received the most recent results of water testing of Darby Elementary School drinking water outlets. Of the 159 outlets initially tested, eight outlets continue to test higher than 15 Parts Per Billion (ppb) screening level for lead which is a level designated by the Environmental Protection Agency (EPA) to take action with additional testing and corrective measures. Lead in drinking water may come from the existing plumbing inside buildings including fittings, solder, water coolers or water faucets. Lead is more likely to be found in drinking water when the water has not been run for an extended period of time and has been sitting in the system.

The lead levels were higher than the EPA-recommended screening level at four classroom bubblers in Rooms 257, 258, 259 and 262, and four classroom faucets in Room 262 (Science Lab). After receiving the test results, we immediately took these water sources out of service. None of the hallway drinking fountains at the school exceeded the screening level. Details on the corrective actions we will take to reduce the amount of lead in water at these fixtures will be discussed in an overview of results and actions to be provided upon completion. Enclosures (1) and (2) are Complete Test Results and a Floor Plan of the elementary school that indicates the location of the fixtures that had lead levels higher than the EPA-recommended screening level.

Exceedances in the lead program are not indicative of a public health issue, but rather the sampling is a proactive measure for early identification of potential lead sources so that corrective action can be taken as necessary.

I know this issue may generate more questions than this letter can answer. As such, I invite you to attend the next Town Hall meeting which will be an opportunity for you to speak with medical and environmental representatives, have your questions answered and voice your concerns.

Testing results are also available on the Commander, Navy Installations Command (CNIC) Web site at:
https://www.cnic.navy.mil/regions/cnrj/installations/cfa_sasebo/om/public_works/.html

To learn more about lead in drinking water in schools and day care centers and additional water quality resources please visit:

- EPA (lead in drinking water in schools and day care centers):
https://www.epa.gov/dwreginfo/drinking-water-schools-and-childcare-facilities
- Drinking Water Taste, Odor, and Color:
http://water.epa.gov/drink/contaminants/secondarystandards.cfm
- CFAS Annual Drinking Water Consumer Confidence Report:
https://www.cnic.navy.mil/regions/cnrj/installations/cfa_sasebo/om/public_works/.html

If you have any concerns at all, please contact my Environmental Team, Ms. Elizabeth Barris (DSN: 315-252-3369 or e-mail: elizabeth.barris@fe.navy.mil) or Mr. Frederick S. Pianalto (DSN: 315-252-3263 or e-mail: frederick.pianalto@fe.navy.mil).

If you have any health related questions or concerns, I encourage you to contact your health care provide or if you are a TRICARE beneficiary, use the REGION Appointment Center to schedule an appointment with your primary care provider at Commercial: 1-866-645-4584.

Rest assured that my team and I will continue to monitor and test water quality at the Darby Elementary School to ensure our drinking water lead levels are lower than the EPA-recommended screening levels. I am committed to the safety and health of all personnel and family members using our facilities and will keep you updated on this issue.

Sincerely,

B. L. STALLINGS
Captain, U.S. Navy
Commander,
Fleet Activities Sasebo

Enclosures: 1. Summary of Results
2. Darby Elementary School Floor Plan of Areas with Exceedances

Copy to: CNIC N45
NAVFAC N45

Table 1. Summary of Results — Derby Elementary - Hario

SAMPLING LOCATION DESCRIPTION				INITIAL SAMPLING RESULTS			RE-SAMPLING RESULTS				CORRECTIVE ACTIONS	POST REMEDIATION SAMPLING RESULTS	
				Recommeded Level = 15 parts per billion (ppb)								Recommeded Level = 20ppb	
CATEGORY Water Intended For:	SAMPLE ID	Room Number - Outlet Description	Comments	First Draw (ppb)	Retest required?	Date Fixture Secured? (See Note 1)	Water Fountain 15 min. Follow up Flush Sample - Collected day before First Draw Sampling (ppb)	First Draw (ppb)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)	Combined Costs	Description	First Draw (ppb) (See note 2)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)
SAMPLING DATE				6/18/2019			N/A	9/14/2019	9/14/2019				
RESULTS DATE				8/28/2019			N/A	10/17/2019	10/17/2019				
WASHING	5114-F-1-19	104 NURSE OFFICE	FAUCET	0.69	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-2-19	105 TEACHERS LOUNGE	FAUCET	0.82	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-3-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-5-19	112 TOILET	FAUCET	4.5	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-6-19	112 TOILET	FAUCET	5.1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-7-19	112 TOILET	FAUCET	2.3	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-8-19	113 TOILET	FAUCET	1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-9-19	113 TOILET	FAUCET	0.93	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-10-19	113 TOILET	FAUCET	0.77	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-11-19	135 KITCHEN IN RM 107	FAUCET	1.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-12-19	109 TOILET	FAUCET	1.6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-13-19	110 TOILET	FAUCET	0.93	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-14-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-15-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-15A-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-16-19	114 STAFF RM	FAUCET	2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-17-19	115 CLASSROOM	FAUCET	4.8	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-18-19	116 TOILET	FAUCET	2.3	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-19-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-20-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-21-19	118 CLASSROOM	FAUCET	1.7	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-22-19	118 CLASSROOM	BUBBLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-23-19	119 CLASSROOM	FAUCET	3.2	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-24-19	119 CLASSROOM	BUBBLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-25-19	120 CLASSROOM	FAUCET	7.2	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-26-19	120 CLASSROOM	BUBBLER	12	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-27-19	121 CLASSROOM	FAUCET	3	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-28-19	121 CLASSROOM	BUBBLER	0.71	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-29-19	123 ART RM	FAUCET	14	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-30-19	123 ART RM	FAUCET	7.1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-31-19	123 ART RM	FAUCET	4.6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-32-19	123 ART RM	FAUCET	1.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-33-19	123 ART RM	FAUCET	3.6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-34-19	123 ART RM	FAUCET	5	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-36-19	124 TOILET	FAUCET	1.3	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-37-19	125 SUPPLY OFFICE	FAUCET	2.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-38-19	126 SUPPLY STORAGE	FAUCET	1.9	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-41-19	128 MAIN KITCHEN	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-42-19	128 MAIN KITCHEN	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-43-19	128 MAIN KITCHEN	FAUCET	1.4	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-44-19	128 MAIN KITCHEN	FAUCET	0.57	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-45-19	128 MAIN KITCHEN	FAUCET	1.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-46-19	142 LOCKER RM IN RM 128	FAUCET	1.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-50-19	151 TOILET	FAUCET	0.76	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-51-19	152 TOILET	FAUCET	0.62	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-52-19	153 TOILET	FAUCET	1.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-53-19	154 TOILET	FAUCET	1.4	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-54-19	N/A HALLWAY NEXT TO	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C-55-19	N/A HALLWAY NEXT TO	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-56-19	156 CLASSROOM	FAUCET	0.58	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-57-19	156 CLASSROOM	FAUCET	0.5	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-58-19	156 CLASSROOM	FAUCET	1.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-60-19	156 CLASSROOM	FAUCET	1.8	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-61-19	156 CLASSROOM	FAUCET	1.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-62-19	156 CLASSROOM	FAUCET	5.8	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-63-19	156 CLASSROOM	BUBBLER	0.72	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-64-19	171 PREPARATION RM IN RM	FAUCET	9.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-65-19	158 CLASSROOM	FAUCET	3.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-66-19	158 CLASSROOM	FAUCET	0.61	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-67-19	158 CLASSROOM	FAUCET	0.57	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-70-19	158 CLASSROOM	FAUCET	2.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-71-19	158 CLASSROOM	FAUCET	2.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-72-19	158 CLASSROOM	FAUCET	7	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-73-19	158 CLASSROOM	BUBBLER	1.4	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-74-19	173 PREPARATION RM IN RM	FAUCET	5.8	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-75-19	159 CLASSROOM	FAUCET	17	Yes	9/4/2019	N/A	1.8	0.75				
WASHING	5114-F-76-19	159 CLASSROOM	FAUCET	11	NO	N/A	N/A	N/A	N/A				

Table 1. Summary of Results | Darby Elementary - Hario

SAMPLING LOCATION DESCRIPTION				INITIAL SAMPLING RESULTS			RE-SAMPLING RESULTS				CORRECTIVE ACTIONS	POST REMEDIATION SAMPLING RESULTS	
				Recommeded Level = 15 parts per billion (ppb)								Recommeded Level = 20ppb	
CATEGORY Water Intended For:	SAMPLE ID	Room Number - Outlet Description	Comments	First Draw (ppb)	Retest required?	Date Fixture Secured? (See Note 1)	Water Fountain 15 min. Follow up Flush Sample - Collected day before First Draw Sampling (ppb)	First Draw (ppb)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)	Combined Costs	Description	First Draw (ppb) (See note 2)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)
SAMPLING DATE				6/18/2019			N/A	9/14/2019	9/14/2019				
RESULTS DATE				8/28/2019			N/A	10/17/2019	10/17/2019				
WASHING	5114-F-77-19	159 CLASSROOM	FAUCET	19	Yes	9/4/2019	N/A	1.5	0.54				
DRINKING	5114-B-78-19	159 CLASSROOM	BUBBLER	51	Yes	9/4/2019	N/A	2.6	0.79				
WASHING	5114-F-79-19	159 CLASSROOM	FAUCET	2.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-80-19	159 CLASSROOM	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-81-19	159 CLASSROOM	FAUCET	0.85	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-83-19	175 PREPARATION RM IN RM	FAUCET	17	Yes	9/4/2019	N/A	1.9	0.5				
WASHING	5114-F-84-19	160 CLASSROOM	FAUCET	17	Yes	9/4/2019	N/A	2.9	N.D.				
DRINKING	5114-B-85-19	160 CLASSROOM	BUBBLER	4.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-86-19	161 CLASSROOM	FAUCET	1.6	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-87-19	161 CLASSROOM	BUBBLER	2.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-88-19	162 CLASSROOM	FAUCET	3.4	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-89-19	162 CLASSROOM	BUBBLER	9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-90-19	164 TEACHERS LOUNGE	FAUCET	5.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-91-19	N/A OUTSIDE FAUCET BY 105	FAUCET	1.1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-92-19	N/A OUTSIDE FAUCET BY 106	FAUCET	8.4	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-93-19	N/A OUTSIDE FAUCET BY 115	FAUCET	5.1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-94-19	N/A OUTSIDE FAUCET BY 119	FAUCET	2.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-95-19	N/A OUTSIDE FAUCET BY 144	FAUCET	0.66	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-96-19	N/A OUTSIDE FAUCET BY 125	FAUCET	1.3	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-97-19	N/A OUTSIDE FAUCET BY 128	FAUCET	1.4	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-99-19	N/A OUTSIDE FAUCET BY 128	FAUCET	6.8	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-100-19	N/A OUTSIDE BUBBLER BY 156	BUBBLER	2.8	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B-101-19	N/A OUTSIDE BUBBLER BY 158	BUBBLER	100	Yes	9/4/2019	N/A	9.73	1.6				
WASHING	5114-F-102-19	N/A OUTSIDE FAUCET BY 158	FAUCET	6.3	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-103-19	N/A OUTSIDE FAUCET BY 158	FAUCET	11	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-104-19	N/A OUTSIDE FAUCET BY	FAUCET	12	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-105-19	105 TOILET IN RM 105	FAUCET	0.95	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-106-19	105 TOILET IN RM 105	FAUCET	0.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-107-19	N/A OUTSIDE FAUCET BY 121	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
COOKING	5114-F-108-19	128 MAIN KITCHEN	FAUCET	1.6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-110-19	152 TOILET	FAUCET	1.6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F-111-19	153 TOILET	FAUCET	0.99	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-1-19	201 CLASSROOM	FAUCET	6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-2-19	202 CLASSROOM	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-3-19	203 CLASSROOM	FAUCET	0.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-4-19	207 CLASSROOM	FAUCET	1.5	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-5-19	208 CLASSROOM	FAUCET	0.66	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-8-19	212 TOILET	FAUCET	0.85	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-9-19	212 TOILET	FAUCET	0.63	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-10-19	212 TOILET	FAUCET	0.96	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-11-19	212 TOILET	FAUCET	4.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-12-19	213 TOILET	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-13-19	213 TOILET	FAUCET	4.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-14-19	213 TOILET	FAUCET	1.2	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-15-19	213 TOILET	FAUCET	3.5	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C1-16-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C1-16A-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-17-19	228 HOST NATION RM	FAUCET	0.92	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-19-19	216 TOILET	FAUCET	0.91	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C1-20-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-21-19	218 CLASSROOM	FAUCET	2.5	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B1-22-19	218 CLASSROOM	BUBBLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-23-19	221 CLASSROOM	FAUCET	3.4	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B1-24-19	221 CLASSROOM	BUBBLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-25-19	222 TEACHERS RM	FAUCET	1.8	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-26-19	223 CLASSROOM	FAUCET	5.2	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B1-27-19	223 CLASSROOM	BUBBLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F1-28-19	224 TOILET	FAUCET	1.7	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C1-29-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-C2-4-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-5-19	252 TOILET	FAUCET	2.3	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-6-19	252 TOILET	FAUCET	0.55	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-7-19	252 TOILET	FAUCET	0.72	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-8-19	253 TOILET	FAUCET	1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-9-19	253 TOILET	FAUCET	N.D.	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-10-19	253 TOILET	FAUCET	0.71	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-11-19	256 CLASSROOM	FAUCET	7.7	NO	N/A	N/A	N/A	N/A				

Table 1. Summary of Results — Darby Elementary - Hario

SAMPLING LOCATION DESCRIPTION				INITIAL SAMPLING RESULTS			RE-SAMPLING RESULTS				CORRECTIVE ACTIONS	POST REMEDIATION SAMPLING RESULTS	
				Recommeded Level = 15 parts per billion (ppb)								Recommeded Level = 20ppb	
CATEGORY Water Intended For:	SAMPLE ID	Room Number - Outlet Description	Comments	First Draw (ppb)	Retest required?	Date Fixture Secured? (See Note 1)	Water Fountain 15 min. Follow up Flush Sample - Collected day before First Draw Sampling (ppb)	First Draw (ppb)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)	Combined Costs	Description	First Draw (ppb) (See note 2)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)
SAMPLING DATE				6/18/2019			N/A	9/14/2019	9/14/2019				
RESULTS DATE				8/28/2019			N/A	10/17/2019	10/17/2019				
DRINKING	5114-B2-12-19	256 CLASSROOM	BUBBLER	4.7	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-13-19	257 CLASSROOM	FAUCET	2.8	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B2-14-19	257 CLASSROOM	BUBBLER	18	Yes	9/4/2019	N/A	18	2.7				
WASHING	5114-F2-15-19	258 CLASSROOM	FAUCET	8.3	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B2-16-19	258 CLASSROOM	BUBBLER	32	Yes	9/4/2019	N/A	33	3.6				
WASHING	5114-F2-17-19	273 PREPARATION RM IN RM	FAUCET	10	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-18-19	259 CLASSROOM	FAUCET	7.7	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B2-19-19	259 CLASSROOM	BUBBLER	28	Yes	9/4/2019	N/A	31	7.4				
WASHING	5114-F2-20-19	275 PREPARATION RM IN RM	FAUCET	4	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-21-19	260 CLASSROOM	FAUCET	2.7	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B2-22-19	260 CLASSROOM	BUBBLER	4.9	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-23-19	261 CLASSROOM	FAUCET	3.3	NO	N/A	N/A	N/A	N/A				
DRINKING	5114-B2-24-19	261 CLASSROOM	BUBBLER	12	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-25-19	262 SCIENCE RM	FAUCET	34	Yes	9/4/2019	N/A	21	1.6				
WASHING	5114-F2-26-19	262 SCIENCE RM	FAUCET	22	Yes	9/4/2019	N/A	16	1.3				
WASHING	5114-F2-27-19	262 SCIENCE RM	FAUCET	17	Yes	9/4/2019	N/A	8.3	1.5				
WASHING	5114-F2-28-19	262 SCIENCE RM	FAUCET	13	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-29-19	262 SCIENCE RM	FAUCET	9.6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-30-19	262 SCIENCE RM	FAUCET	6.1	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-31-19	262 SCIENCE RM	FAUCET	20	Yes	9/4/2019	N/A	17	1.9				
DRINKING	5114-B2-32-19	262 SCIENCE RM	BUBBLER	34	Yes	9/4/2019	N/A	42	3.2				
WASHING	5114-F2-33-19	265 SCIENCE PREPARATION	FAUCET	6	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-34-19	266 STAFF RM	FAUCET	7.4	NO	N/A	N/A	N/A	N/A				
WASHING	5114-F2-35-19	262 SCIENCE RM	FAUCET	34	Yes	9/4/2019	N/A	30	2.8				
DRINKING	5114-C2-3-19	N/A HALLWAY NEXT TO RM	COOLER	N.D.	NO	N/A	N/A	N/A	N/A				

Notes:

[1] Affected outlets were immediately secured after receiving verbal communication from the lab on results exceeding the recommended level of 15 ppb.

[2] Post-remediation sampling was initially conducted on [ENTER DATE]. Additional [CORRECTIVE ACTIONS DESCRIPTION] were implemented and final results below recommended level of 15 ppb for sample collected on [ENTER DATE] are shown on the table.

Table 2. Summary Statistics

CATEGORY	INITIAL SAMPLING RESULTS		RE-SAMPLING RESULTS				POST REMEDIATION RESULTS
	Recommeded Level = 15 parts per billion (ppb)						
	First Draw (ppb)			First Draw (ppb)	Follow up Flush - Collected 30 seconds after First Draw Sampling (ppb)		First Draw (ppb)
Total Drinking	36			6	6		
Total Drinking > 15 ppb	6			4	0		
Total Cook/Brush	7			0	0		
Total Cook/Brush > 15 ppb	0			0	0		
Total Washing	116			9	9		
Total Washing > 15 ppb	9			4	0		
Total Samples	159			15	15		
Total Samples > 15 ppb	15			8	0		

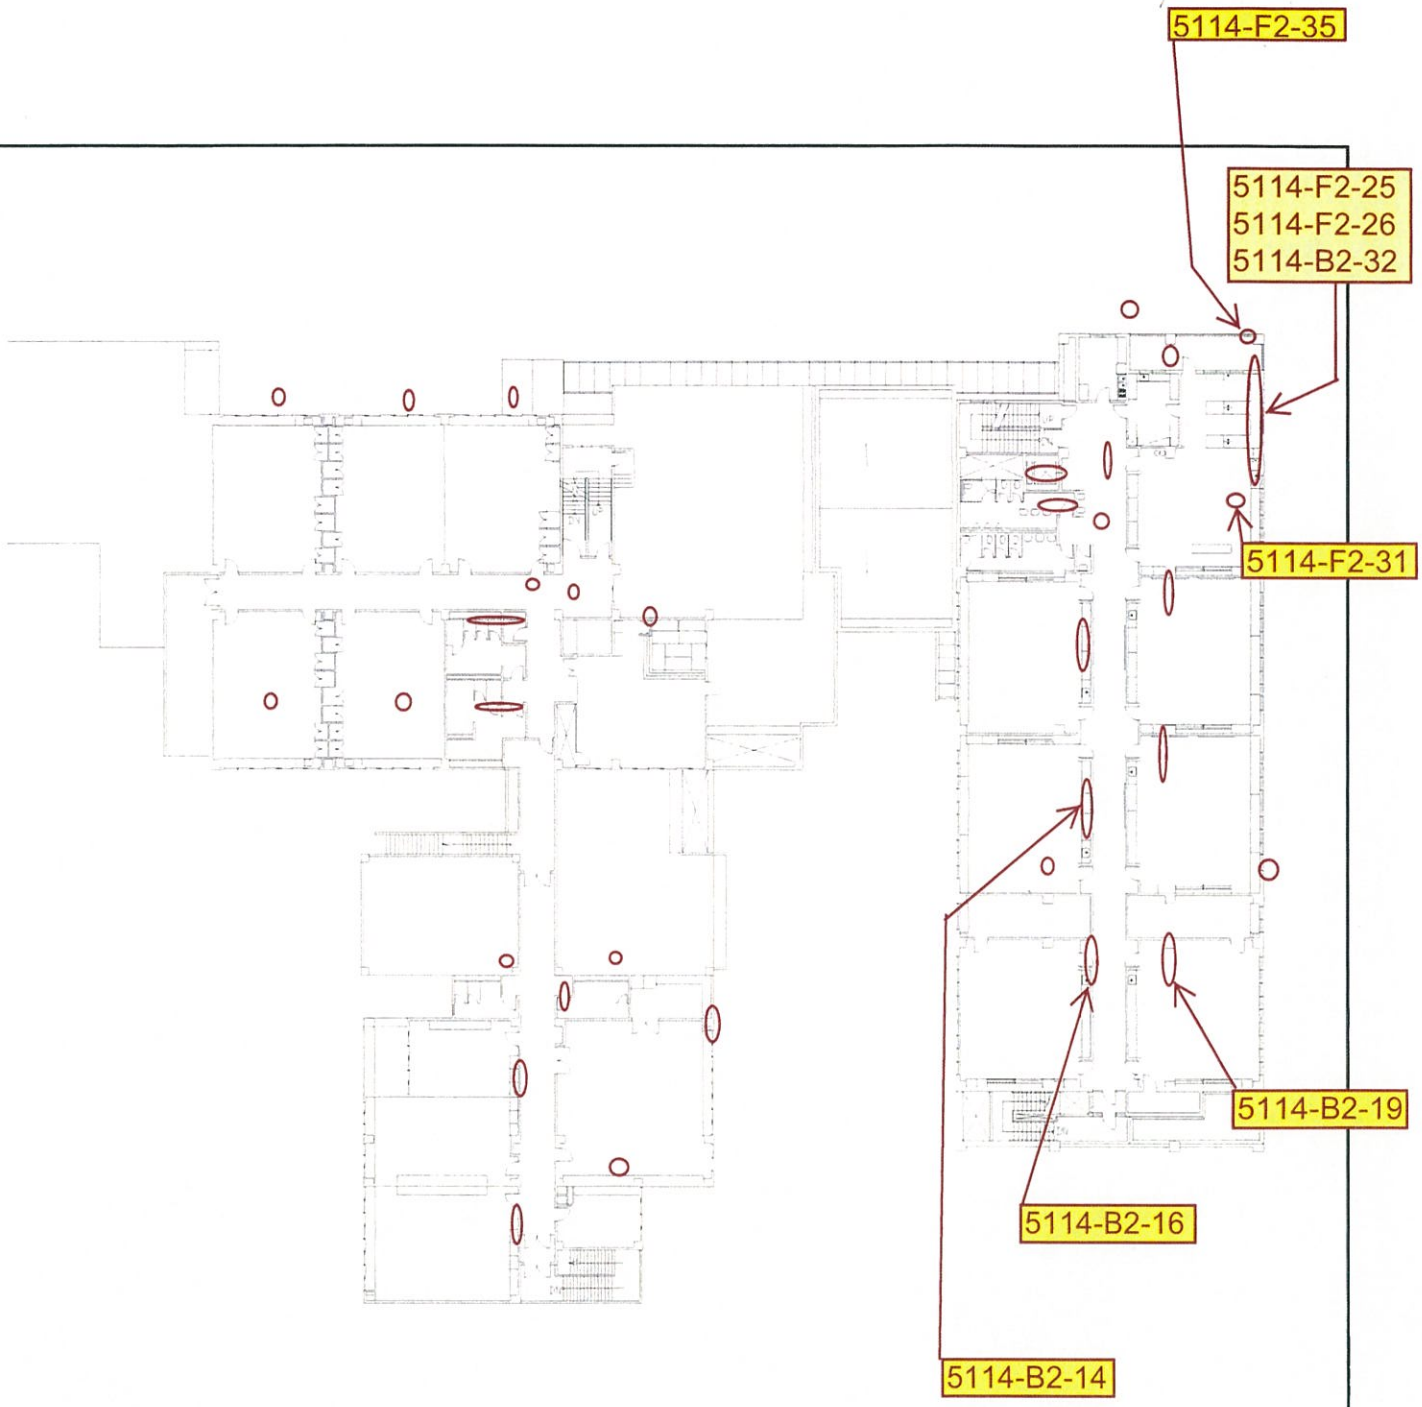

2nd FLOOR PLAN: BLDG.#5114

Red Circles indicate all initial sampling locations

5114-B2-14 Yellow Boxes indicate location and ID number of fixtures requiring additional corrective actions

KEY NO.	TITLE		PUBLIC WORKS DEPT. U.S. FLEACT SASEBO JAPAN	
	SATISFACTORY TO	SKETCHED BY	SUPV	
			FAC.DIV.DIR	
	APPROVED	CONTRACT NO. N62836-	SHT. NO.	PWD DWG NO.

Enclosure (2)
